




Act ID	Description	Orig Dur	Rev Dur	Early Start	Early Finish	Total Float	Predecessors	Successors
140D	FG AND PLACE 8" GRAVEL AROUND TANK	1d	1d	02FEB27	02FEB27	142d 130D, 135D	145D	
145D	INSTALL REMOVABLE STEEL BOLLARDS	1d	1d	03FEB27	03FEB27	142d 140D	150D	
150D	EX/BACKFIL FOR JOINT TRENCH UTILITIES	1d	1d	04FEB27	04FEB27	142d 145D	160D	
160D	RW TANK ELECTRICAL/INSTRUMENTATION	10d	10d	05FEB27	19FEB27	142d 150D, 280B	165D	
165D	PAINT EXPOSED PIPING/APPT	2d	2d	22FEB27	23FEB27	142d 160D	110U	
SEWER IMPROVEMENTS								
100E	SANITARY SEWER IMPV LITTLE LAKE RD TO SCHOOL ST	4d	0	01MAY26 A	06MAY26 A			
102E	SANITARY SEWER IMPV SCHOOL TO HWY 1	2d	0	07MAY26 A	12MAY26 A	100E		
105E	TEST SEWER SYSTEM	2d	2d	15JUN26	22JUN26	311d 100E, 102E	110E	
110E	RAISE SSMH TO GRADE	1d	1d	23JUN26	23JUN26	311d 105E	110U	
FRIENDSHIP PARK IRRIGATION IMPV								
100F	CONSTRUCT IRRIGATION SYSTEM	10d	10d	24AUG26 *	04SEP26	0 130C	105F	
105F	CONSTRUCT RW SIGNS	2d	2d	08SEP26	09SEP26	256d 100F, 350B	110U	
WWTP AREATION BASIN PHASED IMPV								
100G	PREP FOR BASIN SHUTDOWN (FRAC TANKS) VAC TRUCKS	0	0	13JUL26 *		0	105G	
105G	DAY 1 MCCSD	1d	1d	13JUL26 *	13JUL26	0 100G	110G	
110G	DAY 2 REMOVE GRIT/WASH DOWN BASIN REMOVE AIR TUB	1d	1d	14JUL26	14JUL26	95d 105G	115G	
115G	DAY 3 ANOXIC BAFFLE, (CCB BAFFLE ALP LATER DATE	1d	1d	15JUL26	15JUL26	95d 110G, 325B	120G	
120G	DAY 3 REINSTALL AIR TUBES & RISERS (5 EACH)	1d	1d	15JUL26	15JUL26	95d 115G	125G	
125G	DAY 4 MCCSD REINSTAE BASIN OPERATION	1d	1d	16JUL26	16JUL26	95d 120G	130G	
130G	DAY 5 MCCSD TO MONITOR OPERATION, DEMOB FRAC TAN	1d	1d	17JUL26	17JUL26	95d 125G	135G	
135G	DAY 5 INSTALL/STARUP ANOXIC MIXER	1d	1d	20JUL26	20JUL26	95d 130G	140G	
140G	DAY 6 TRANSFER GIRT DRYING BEDS TO MCCSD BINS	1d	1d	21JUL26	21JUL26	95d 135G	145G	
145G	COMMENCE AIR LIFT PUMP COMMISSIONING (2 WEEKS)	10d	10d	19OCT26	30OCT26	33d 140G, 330B	100H, 100M	
CHLORINE CONTACT BASIN								
100H	STRUCTURAL EX. CCB FOOT PRINT/SG PREP BOTTOM	3d	3d	02NOV26	04NOV26	33d 145G	105H	
105H	PLACE & COMPACT BASE ROCK CCB BASE	1d	1d	08NOV26	08NOV26	33d 100H	110H	
110H	F/S SUMP SLAB & STARTER WALL	2d	2d	09NOV26	09NOV26	33d 105H	112H	
112H	SET REBAR FOR SUMP SLAB	1d	1d	10NOV26	10NOV26	33d 110H	115H	
115H	POUR SUMP SLAB & STARTER WALLS	1d	1d	11NOV26	11NOV26	33d 112H	120H	
120H	F/S BOTTOM SLAB & STARTER WALL	5d	5d	12NOV26	18NOV26	33d 115H	122H	
122H	SET REBAR FOR BOTTOM SLAB	5d	5d	19NOV26	25NOV26	33d 120H	125H	
125H	POUR BOTTOM SLAB & STARTER WALLS	1d	1d	25NOV26	25NOV26	33d 122H	130H	
130H	F/S PERMITTER WALLS & INTERIOR WEIR WALL	17d	17d	30NOV26	22DEC26	33d 125H	132H	
132H	SET REBAR FOR PERMITTER & INTERIOR WEIR WALLS	10d	10d	23DEC26	07JAN27	33d 130H	135H	
135H	POUR PERMITTER WALLS	1d	1d	08JAN27	08JAN27	33d 132H	140H	
140H	POUR WIER WALLS	1d	1d	08JAN27	08JAN27	33d 135H	145H, 167H	
145H	PLACE/REMOVE SHORING & SET SOFFIT FOR ROOF	14d	14d	11JAN27	28JAN27	33d 140H	150H	
150H	F/S BEAMS FOR ROOF SLAB	6d	6d	25JAN27	05FEB27	33d 145H	152H	
152H	SET REBAR FOR ROOF SLAB	5d	5d	08FEB27	12FEB27	33d 150H	155H	
155H	SET SCREEDS/INSTALL GRATES & BULK HEADS	6d	6d	16FEB27	23FEB27	33d 152H, 290B	160H	
160H	POUR ROOF SLAB	1d	1d	24FEB27	24FEB27	33d 155H	165H	
165H	CLASS 1 FINISH	15d	15d	25FEB27	17MAR27	33d 160H	170H	
167H	BACKFILL & COMPACT CCB	3d	3d	11JAN27	13JAN27	160d 140H	100I	
170H	SET REBAR FOR INTERIOR FILLETS	1d	1d	18MAR27	18MAR27	33d 165H	175H	
175H	F/P/F FILLETS	2d	2d	19MAR27	22MAR27	33d 170H	180H	
180H	INSTALL FRP BAFFLES	2d	2d	23MAR27	24MAR27	33d 175H, 360B	185H	
185H	INSTALL CHLOR ANALYZER & SAMPLE PUMP	2d	2d	25MAR27	26MAR27	33d 180H, 310B	190H	
190H	LEAKAGE TEST CC BASIN	2d	2d	29MAR27	30MAR27	33d 185H	100T, 195H	
195H	REPLANT LAWN AREA	1d	1d	30MAR27	30MAR27	117d 190H	110U	
WWTP UTILITYT IMPV								
100I	CONSTRUCT 10" RWM, FH, CV/VAULT	3d	3d	14JAN27	18JAN27	160d 167H	105I	
105I	CONSTRUCT 2" FE/FRP VAULT IMPV	4d	4d	19JAN27	22JAN27	160d 100I, 345B	100Q, 110I	
110I	HYDROSTAIC TESTING	1d	1d	26JAN27	26JAN27	160d 100Q, 105I	115I	
115I	SITE RESTORATION, PAVE/CONCRETE SW	1d	1d	27JAN27	27JAN27	160d 110I	110U	
CHLORINE GENERATION SYSTEM								
100J	CONSTRUCT CONCRETE EQUIPMENT PADS	2d	2d	31DEC26	04JAN27	167d 300B	105J	
105J	CONSTRUCT GENERATION SYSTEM IN GARAGE	11d	11d	05JAN27	19JAN27	167d 100J, 302B	100K	
COAGULANT DOSING SYSTEM								
100K	CONSTRUCT COAGULANT DOSING SYSTEM	4d	4d	20JAN27	25JAN27	167d 105J, 315B	105K	
105K	PAINTING	1d	1d	26JAN27	26JAN27	167d 100K		
PROCESS AIR PIPING, PLUG VALVES								
100L	STAGE 1 REMOVE EX. PROCESS AIR PIPE	2d	2d	02SEP26	03SEP26	179d 305B, 375B	105L	
105L	STAGE 1 CONSTRUCT NEW PROCESS AIR PIPE	2d	2d	04SEP26	08SEP26	179d 100L	110L	
110L	STAGE 1 TEMP TIE INTO EX. PROCESS AIR	1d	1d	09SEP26	09SEP26	179d 105L	115L	
115L	STAGE 1 CORE DRILL BASIN WALLS FOR NEW PAP	1d	1d	10SEP26	10SEP26	179d 110L	117L	
117L	TEST AIR PIPING	1d	1d	10SEP26	10SEP26	179d 115L	120L	
120L	STAGE 2 REMOVE EX. PROCESS AIR PIPE	3d	3d	11SEP26	15SEP26	179d 117L	125L	
125L	STAGE 2 CONSTRUCT NEW PROCESS AIR PIPE	3d	3d	16SEP26	18SEP26	179d 120L	130L	
130L	STAGE 2 TIE INTO EX. PROCESS AIR PIPE	1d	1d	18SEP26	18SEP26	179d 125L	135L	
135L	STAGE 2 CORE DRILL BASIN WALL FOR NEW PAP	1d	1d	21SEP26	21SEP26	179d 130L	140L	
140L	STAGE 2 INSTALL PIPE SUPPORTS	3d	3d	22SEP26	24SEP26	179d 135L	145L	
145L	TEST AIR PIPING	1d	1d	25SEP26	25SEP26	179d 140L	150L	
150L	TIE IN PROCESS AIR PIPE	1d	1d	28SEP26	28SEP26	179d 145L	110U, 140T	
MLR PIPING SYSTEM								
100M	REMOVE EX. MLR PIPING SYSTEM	1d	1d	02NOV26	02NOV26	211d 145G	105M	
105M	CONSTRUCT NEW 8" MLR PIPE	3d	3d	03NOV26	06NOV26	211d 100M	110M	
110M	PAINT 8" MLR UNLESS SS PIPE IS USED	2d	2d	06NOV26	09NOV26	211d 105M	115M	
115M	TEST MLR PIPE	1d	1d	10NOV26	10NOV26	211d 110M	100N	
FILTER BACKWASH SYSTEM								
100N	REMOVE EX. FILTER BACKWASH PIPELINE	2d	2d	11NOV26	12NOV26	211d 115M, 330A	105N	
105N	CONSTRUCT NEW 4" FILTER BACKWASH PIPELINE	2d	2d	13NOV26	16NOV26	211d 100N	110N	
110N	REPAIR CONCRETE WALLS AT PENETRATIONS	1d	1d	17NOV26	17NOV26	211d 105N	115N	
115N	PAINT 4" FB UNLESS SS PIPE IS USED	2d	2d	18NOV26	19NOV26	211d 110N		
RECYCLED WATER DISTRIBUTION PUMPS								
100O	CONSTRUCT RW DISTRIBUTION PUMPS @ CCB	2d	2d	16NOV26	17NOV26	209d 335B	105O	
105O	F/P/S CONCRETE PUMP PAD & RAISED RWP PAD	2d	2d	18NOV26	19NOV26	209d 100O	110O	
110O	CONSTRUCTR 6" MANIFOLD & TIE INTO RW PUMPS	1d	1d	19NOV26	19NOV26	209d 105O	115O	
115O	PAINT EXPOSED PIPE & PUMPS	2d	2d	20NOV26	23NOV26	209d 110O		
RECYCLED WATER TRANSFER PUMPS								
100P	REMOVE & REINSTALL EX. TRANSFER PUMP	1d	1d	04SEP26	04SEP26	257d 340B	105P	
105P	REMOVE I-BEAMS AND CUT OPENING IN STEEL PLATE	1d	1d	08SEP26	08SEP26	257d 100P, 365B	110P	
110P	WELD NEW I-BEAMS ON STEEL PLATE	1d	1d	09SEP26	09SEP26	257d 105P	115P	
115P	CONSTRUCT TRANSFER PUMP & 2" DIST MAIN	2d	2d	10SEP26	11SEP26	257d 110P	120P	
120P	SET ADJUSTABLE PIPE SUPPORT	1d	1d	14SEP26	14SEP26	257d 115P	125P	
125P	PAINT EXPOSED PIPE & PUMP HEAD	2d	2d	15SEP26	16SEP26	257d 120P		
FILTER EFFLUENT SYSTEM								
100Q	2" FILTER EFFLUENT IN JT W/ RW	2d	2d	25JAN27	26JAN27	160d 105I	110I	
AIR MIXER PUMP								
100Q1	CONSTRUCT AIR MIX PUMP ASSEMBLY IN BASIN	2d	2d	15OCT26	16OCT26	167d 330B	150T	
WWTP ELECTRICAL & INSTRUMENTATION								
100R	ELECTRICAL IMPV WWTP	20d	20d	22FEB27	19MAR27	0 285B	105R, 110R	
105R	INSTRUMENTATION IMPV WWTP	40d	40d	22MAR27	14MAY27	0 100R	100T, 100U, 110U	
110R	EX & BACKFILL FOR JOINT TRENCH CONDUIT	2d	2d	22FEB27	23FEB27	142d 100R		
EQUALIZATION BASIN LINER								
100S	MSCCD DRAIN EQUALIZATION BASIN	1d	1d	06JUL26 *	06JUL26	0	105S	
105S	DEMO EXISTING LINER	2d	2d	07JUL26	08JUL26	297d 100S	110S	
110S	MODIFY 16" BASIN INET (3/C-502)	1d	1d	08JUL26	08JUL26	297d 105S	115S	
115S	CONSTRUCT BASIN OUTLET (5/C-502)	1d	1d	09JUL26	09JUL26	297d 110S	120S	
120S	EXCAVATE ANCHOR TRENCH	1d	1d	09JUL26	09JUL26	297d 115S	125S	
125S	BACKFILL ANCHOR TRENCH	1d	1d	09JUL26	09JUL26	297d 120S	130S	
130S	CONSTRUCT NEW BASIN LINER	2d	2d	10JUL26	13JUL26	297d 125S	135S	
135S	SPARK TEST LINER	1d	1d	13JUL26	13JUL26	297d 130S	140S	
140S	MSCCD TO REFLF EQUALIZATION BASIN	1d	1d	13JUL26	13JUL26	297d 135S	110U	
COMMISSIONING & O&M TRAINING TESTING								
100T	RECYCLED WATER DISTRIBUTION SYSTEM START UP	2d	2d	17MAY27	18MAY27	0 105R, 190H	105T	
105T	RECYCLED WATER DIST SYSTEM O&M MANUALS	5d	5d	19MAY27	25MAY27	0 100T	110T	
110T	CHLORINE GENERATION SYSTEM START UP	3d	3d	28MAY27	28MAY27	0 105T	115T	
115T	CHLORINATION GENERATION SYSTEM TRAINING	3d	3d	01JUN27	03JUN27	0 110T	121T	
120T	CHLORINE GENERATION SYSTEM O&M MANUALS	3d	3d	04JUN27	08JUN27	0 115T	121T	
121T	CHLORINE ANALYZER & SAMPLE PUMP START UP	1d	1d	09JUN27	09JUN27	0 120T	122T	
122T	CHLORINE ANALYZER & SAMPLE PUMP TRAINING	1d	1d	10JUN27	10JUN27	0 121T	123T	
123T	CHLORINE ANALYZER & SAMPLE PUMP O&M MANUAL	1d	1d	11JUN27	11JUN27	0 122T	125T	
125T	COAGULANT DOSING SYSTEM START UP	1d	1d	14JUN27	14JUN27	0 123T	130T	
130T	COAGULANT SYSTEM TRAINING	1d	1d	14JUN27	14JUN27	0 125T	135T	
135T	COAGULANT SYSTEM O&M MANUALS	1d	1d	15JUN27	15JUN27	0 130T	140T	
140T	PROCESS AIR SYSTEM START UP	1d	1d	15JUN27	15JUN27	0 135T, 150L	145T	
145T	PROCESS AIR SYSTEM TRAINING	1d	1d	16JUN27	16JUN27	0 140T	150T	
150T	PROCESS AIR SYSTEM O&M MANUALS	1d	1d	17JUN27	17JUN27	0 100Q1, 145T	155T	
RECYCLED WATER DISTRIBUTION SYSTEM START UP								
RECYCLED WATER DIST SYSTEM O&M MANUALS								
CHLORINE GENERATION SYSTEM START UP								
CHLORINATION GENERATION SYSTEM TRAINING								
CHLORINE GENERATION SYSTEM O&M MANUALS								
CHLORINE ANALYZER & SAMPLE PUMP START UP								
CHLORINE ANALYZER & SAMPLE PUMP TRAINING								
CHLORINE ANALYZER & SAMPLE PUMP O&M MANUAL								
COAGULANT DOSING SYSTEM START UP								
COAGULANT SYSTEM TRAINING								
COAGULANT SYSTEM O&M MANUALS								
PROCESS AIR SYSTEM START UP								
PROCESS AIR SYSTEM TRAINING								
PROCESS AIR SYSTEM O&M MANUALS								

Start date	13APR26	Early bar Progress bar Critical bar Summary bar Start milestone point Finish milestone point
Finish date	21SEP27	
Data date	19JUN26	
Run date	23JUN26	
Page number	2A	
© Primavera Systems, Inc.		

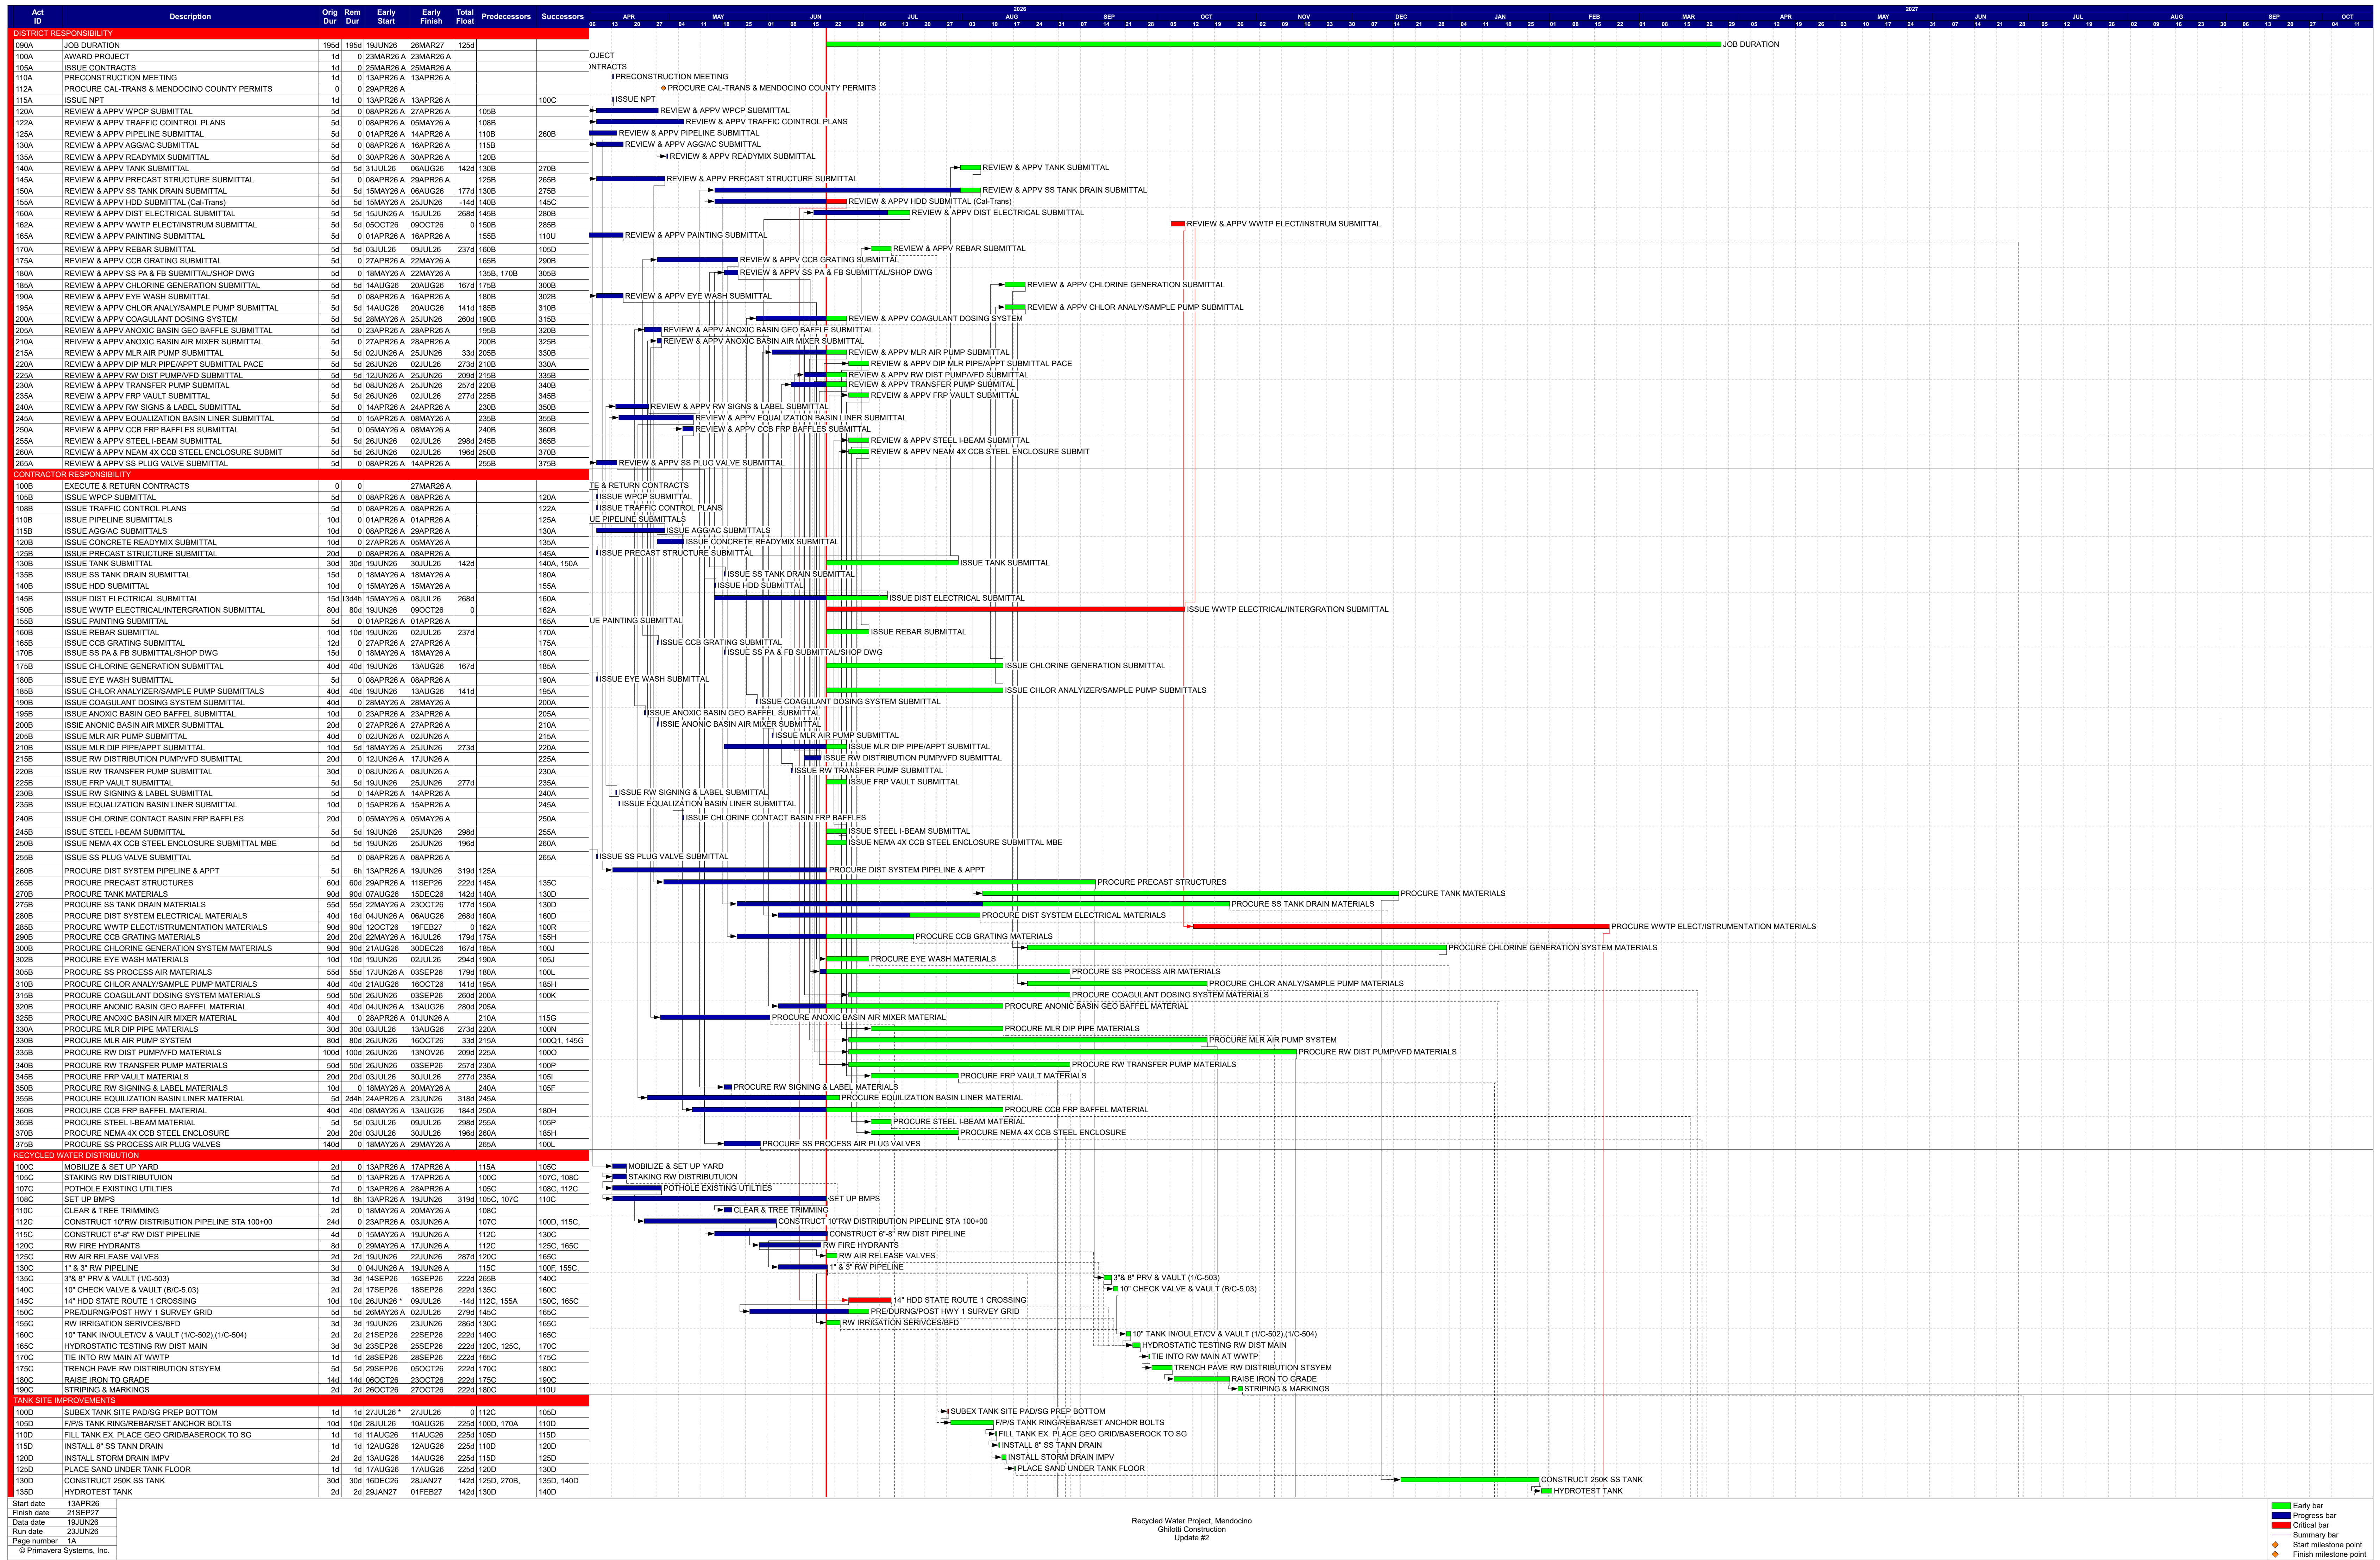
