ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Recycled Water Pipeline Impv**	**51 days**	**Mon 4/13/26**	**Mon 6/22/26**	
2		Potholing	7 days	Mon 4/13/26	Tue 4/21/26	
3		Inclement Weather Delay	3 days	Mon 4/20/26	Wed 4/22/26	
4		10" RW Pipeline from Station 100+00 -136+69	10 days	Thu 4/23/26	Wed 5/6/26	3
5		RW Fire Hydrants (7 each) Westr Side on Hwy 101	4 days	Thu 5/7/26	Tue 5/12/26	4
6		Sanitary Sewer Line Replacement Little Lake Road	9 days	Thu 5/7/26	Tue 5/19/26	4
7		Meet with Cal-Trans to Discuss Scope for HDD	1 day	Wed 5/20/26	Wed 5/20/26	6
8		Set up Hwy 1 Monitoring Grid	1 day	Thu 5/21/26	Thu 5/21/26	7
9		Mobilize HDD/ Excavate Entry & Exit Pits	2 days	Fri 5/22/26	Mon 5/25/26	8
10		Construct HDD under Hwy 1	5 days	Tue 5/26/26	Mon 6/1/26	9
11		10" RW Pipeline from Station 140+95 - 182+00 Little Lake Road	12 days	Wed 5/20/26	Thu 6/4/26	6
12		RW Fire Hydrants (5 each) East Side of Hwy 101	3 days	Mon 5/25/26	Wed 5/27/26	11SS+3 days
13		8" RW Pipeline Kasten St from Station 200+00 -205+00	2 days	Mon 6/15/26	Tue 6/16/26	4
14		3" RW Pipeline Off Kasten ST C-121	1 day	Wed 6/17/26	Wed 6/17/26	13
15		8" RW Pipeline School Street Station 300+00 -303+50	1 day	Thu 6/18/26	Thu 6/18/26	14
16		3" RW Pipeline Off School St to Friendship Park	1 day	Fri 6/19/26	Fri 6/19/26	15
17		1" RW Pipeline to Dog Park	1 day	Mon 6/22/26	Mon 6/22/26	16

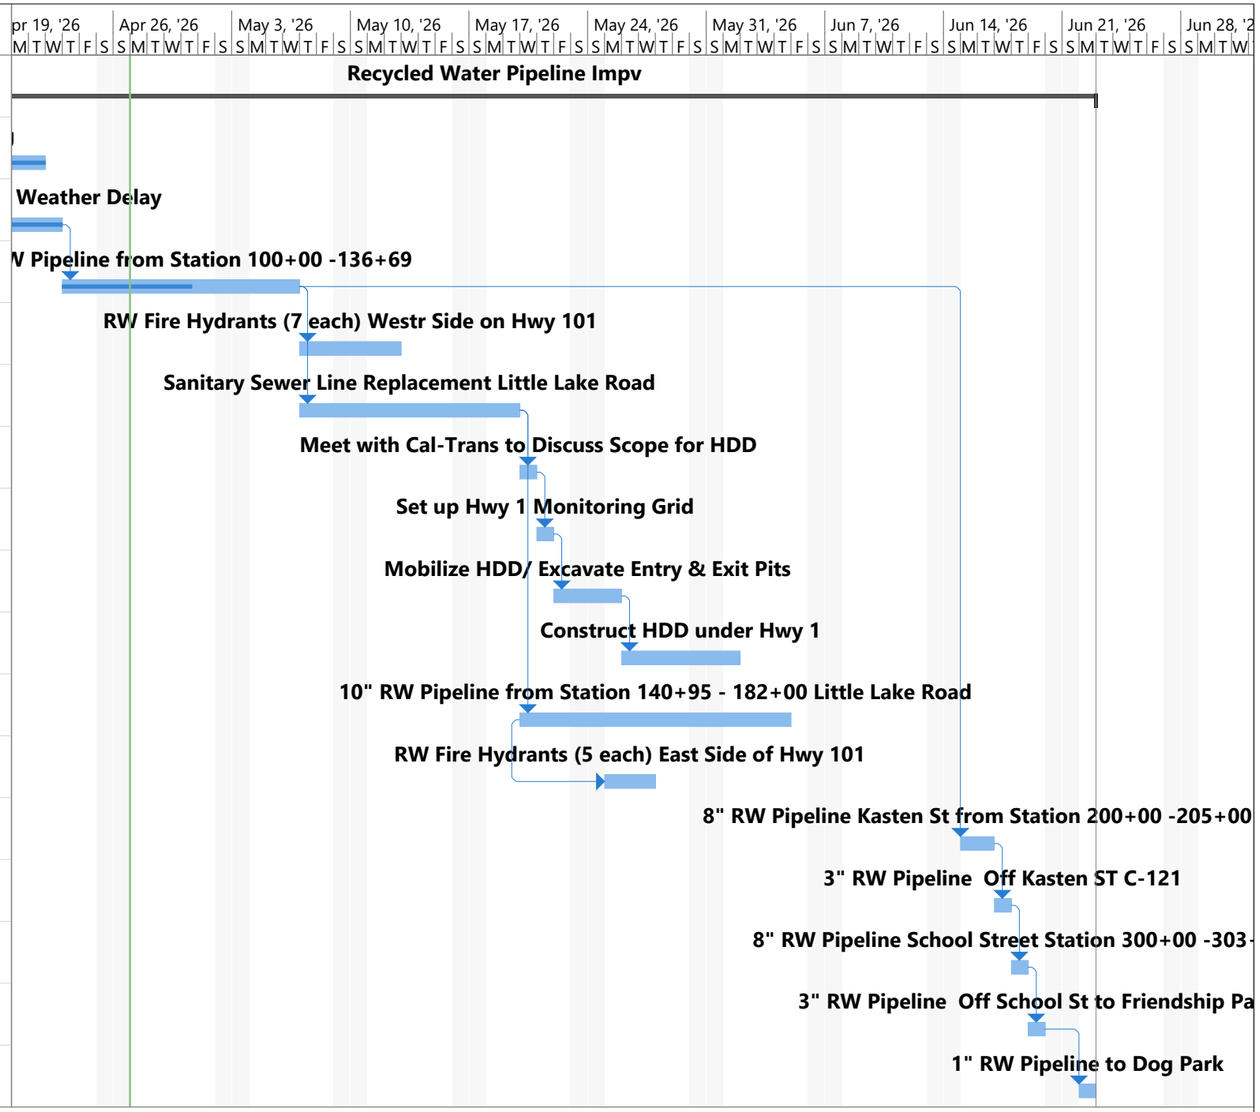

Project: 6200 Look Ahead Sche
Date: Mon 4/27/26

Task	Inactive Task	Manual Summary Rollup	External Milestone	Progress
Split	Inactive Milestone	Manual Summary	Deadline	Manual Progress
Milestone	Inactive Summary	Start-only	Path Successor Milestone Task	
Summary	Manual Task	Finish-only	Path Successor Summary Task	
Project Summary	Duration-only	External Tasks	Path Successor Normal Task	
